

CONSTRUCTION

- Concrete floors will be complete through Level 7 by the end of February.
 - More than 18,000 cubic yards of concrete have been placed.
- More than 850 tons of precast concrete façade panels have been installed.
- More than 50,000 lineal feet of mechanical, plumbing, and sprinkler piping have been run.
- More than 35,000 lineal feet of electrical conduit and wire have been run.
- More than 47 tons of sheet metal ductwork have been installed.
- Approximately 25,000 onsite working manhours are anticipated for the month of February, which would total approximately 221,000 manhours performed for the entire project to date.
- To date, more than 760 people have come onsite for construction.


DESIGN

- The design team is continuing to work through, coordinate, and finalize the design for permitting and construction.
 - 100% construction documents are anticipated to be released in March.
- Building Information Modeling (BIM) coordination between Turner, the design team, and certain Subcontractors is continuing to progress.
 - BIM coordination from Level 14 and below is substantially complete.

SCHEDULE

Construction continues to remain on-schedule!

- Concrete construction (floors, beams, columns) are continuing from Level 7.
- Mechanical, electrical, plumbing, and fire protection conduits, duct, and piping are progressing through Level 3.
- Interior drywall and masonry wall layout and installation are progressing through Level 3.
- Installation of precast concrete façade panels will be complete in March.
- Glass curtainwall panels are in production, with installation to begin soon.
- Three of the six permanent Podium stairwells have been installed.
- Spray-on fireproofing of the structural steel is continuing.
- The temporary construction hoist is operational to Level 5.

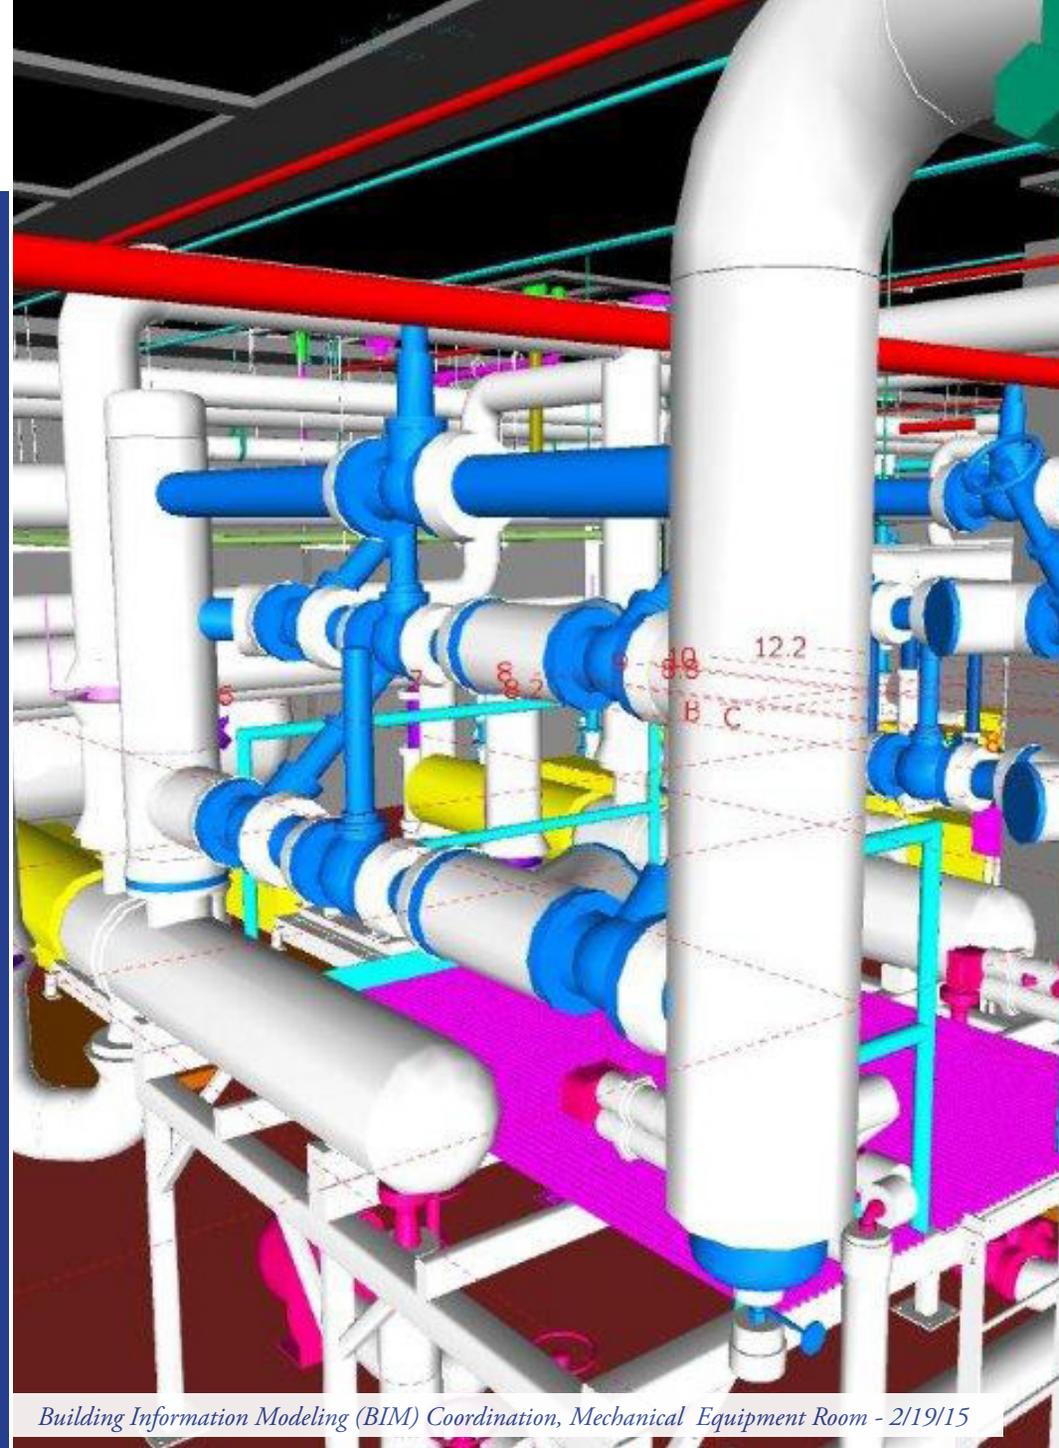

Building Information Modeling (BIM) Coordination, Mechanical Equipment Room - 2/19/15
